

APRIL 2013 HIGHLIGHTS



DREDGING

35,600 cubic yards of lake material removed.



WATER TREATED

74,409,000 gallons of water treated.



CAPPING

2,500 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS

3,000 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

APRIL 1–30, 2013



Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in April 2013	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	35,600 cubic yards	2 million cubic yards*	13.6%
Cap Material Placed	2,500 cubic yards	2.8 million cubic yards*	2.1%
Water Treated	74,409,000 gallons	3 billion gallons*	17%
Wetlands Improved	0 acres	50 acres*	59%
Plants, Shrubs, Trees Planted**	3,000	1.1 million*	16%

*Estimated totals

**Does not include 400,000 shrub willows

Onondaga Lake Dredging and Capping Progress

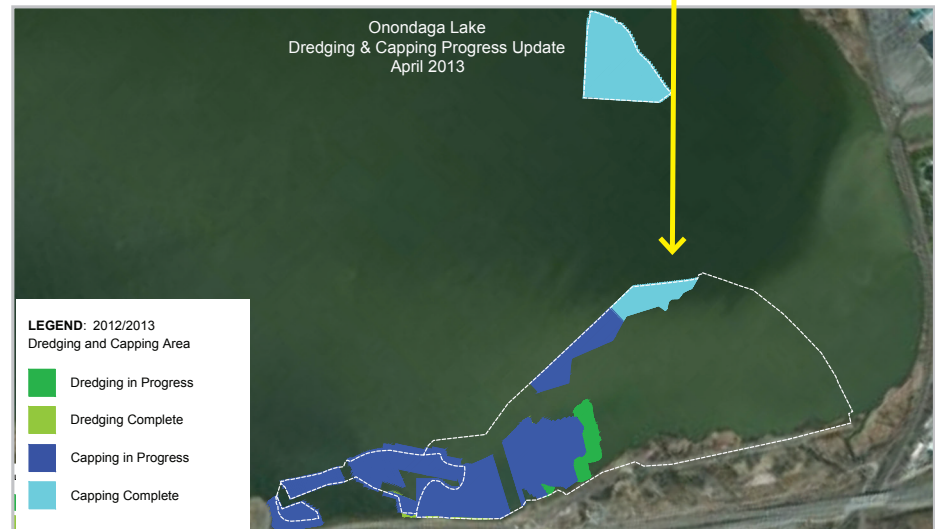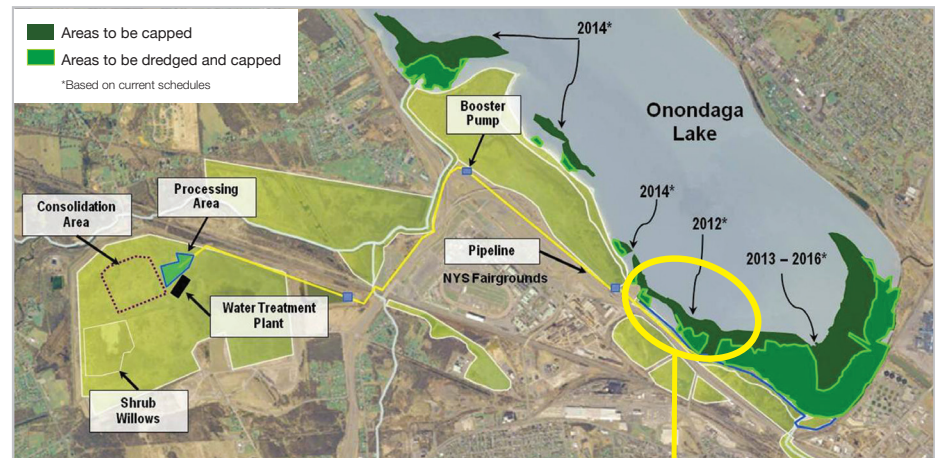

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
