

## APRIL 2017 HIGHLIGHTS



**DREDGING**  
Completed



**WATER TREATED**  
Completed



**CAPPING**  
Completed



**HABITAT / PLANTS / WETLANDS**  
0 plants, shrubs, and trees planted.

# Onondaga Lake Cleanup Progress

APRIL 1 – APRIL 30, 2017

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in April 2017	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	Complete	2.2 million cubic yards	100%
Cap Material Placed	Complete	3.097 million cubic yards	100%
Water Treated	Complete	2.46 billion gallons	100%
Wetlands Improved	0 acres	87 acres*	85%
Plants, Shrubs, Trees Planted**	0 plants	1.1 million*	54%

\*Estimated totals

\*\*Does not include 750,000 shrub willows

## Onondaga Lake Dredging and Capping Progress

LEGEND 2012/2013/2014

■ Dredging in Progress

■ Dredging Complete

--- Dredge Areas




LEGEND 2012/2013/2014/2015/2016

■ Capping in Progress

■ Capping Complete

--- Cap Areas

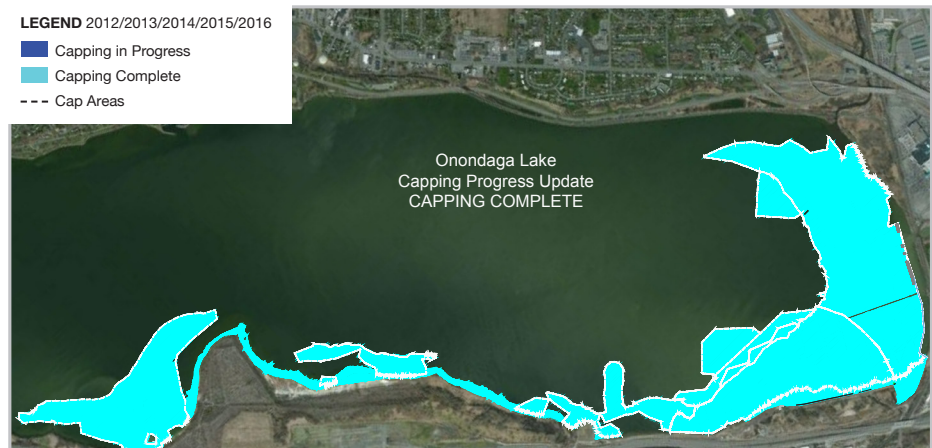

**Honeywell**

For more information, please contact Honeywell at 315.552.9784, or visit [www.lakecleanup.com](http://www.lakecleanup.com).
