

## AUGUST 2012 HIGHLIGHTS



### DREDGING

86,300 cubic yards of lake material removed.



### WATER TREATED

133,825,000 gallons of water treated.



### CAPPING

2,500 cubic yards of capping material placed.



### HABITAT / PLANTS / WETLANDS

32,000 plants, shrubs, and trees planted.

## Onondaga Lake Cleanup Progress

AUGUST 1–31, 2012


Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in August 2012	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	86,300 cubic yards	2 million cubic yards*	4.3%
Cap Material Placed	2,500 cubic yards	2.8 million cubic yards*	0.1%
Water Treated	133,825,000 gallons	3 billion gallons*	5.3%
Wetlands Improved	0 acres	50 acres*	39%
Plants, Shrubs, Trees Planted**	32,000	1.1 million*	12%

\*Estimated totals

\*\*Does not include 400,000 shrub willows

## Onondaga Lake Dredging and Capping Progress

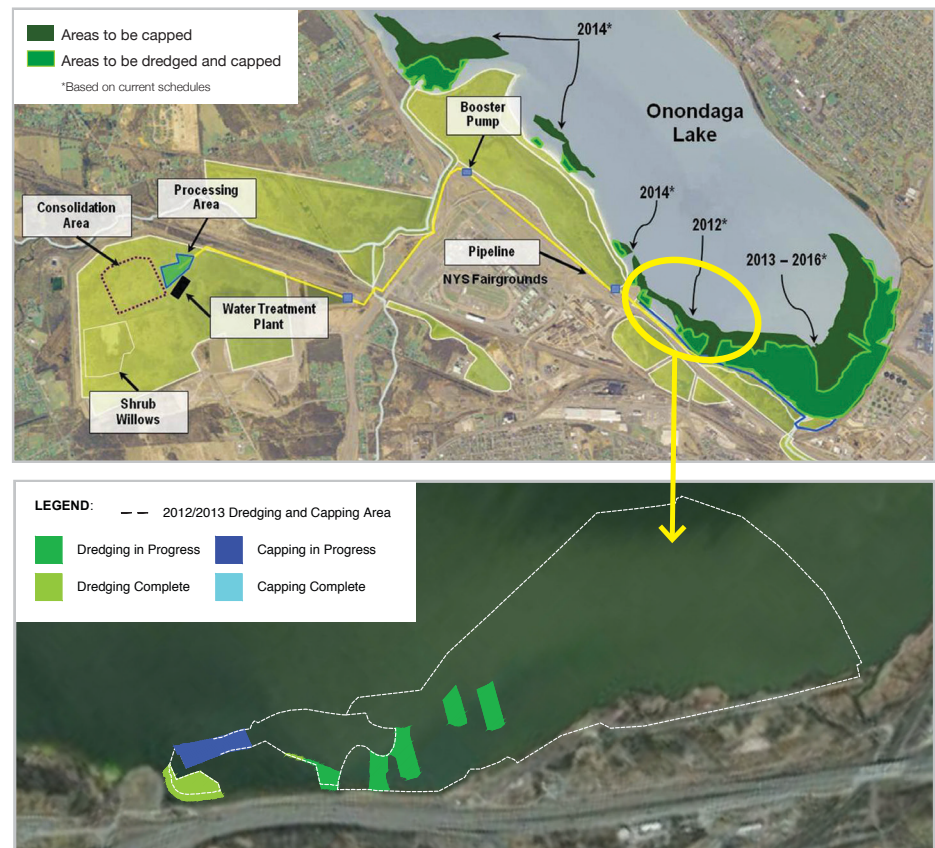

**Honeywell**

For more information, please contact Honeywell at 315.552.9784, or visit [www.lakecleanup.com](http://www.lakecleanup.com).
