

FEBRUARY 2014 HIGHLIGHTS



DREDGING

10,000 cubic yards of lake material removed.



WATER TREATED

14,000,000 gallons of water treated.



CAPPING

10,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS

0 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

FEBRUARY 1 – FEBRUARY 28, 2014


Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in February 2014	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	10,000 cubic yards	2 million cubic yards*	61%
Cap Material Placed	10,000 cubic yards	2.8 million cubic yards*	20%
Water Treated	14,000,000 gallons	2.8 – 3.1 billion gallons*	61%
Wetlands Improved	0 acres	50 acres*	64%
Plants, Shrubs, Trees Planted**	0 plants	1.1 million*	20%

*Estimated totals

**Does not include 400,000 shrub willows

Onondaga Lake Dredging and Capping Progress

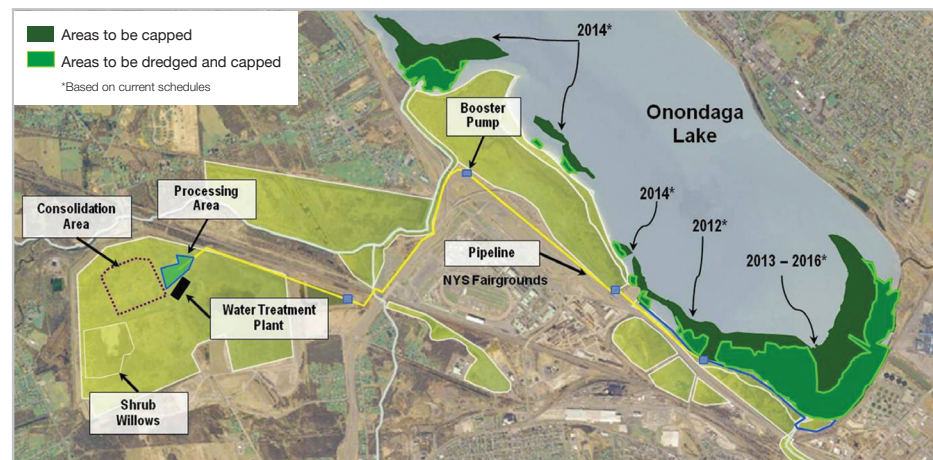

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
