

## JANUARY 2013 HIGHLIGHTS



### DREDGING

0 cubic yards of lake material removed.



### WATER TREATED

12,852,000 gallons of water treated.



### CAPPING

0 cubic yards of capping material placed.



### HABITAT / PLANTS / WETLANDS

6,000 plants, shrubs, and trees planted.

# Onondaga Lake Cleanup Progress

JANUARY 1–31, 2013


Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in January 2013	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	0 cubic yards	2 million cubic yards*	11.8%
Cap Material Placed	0 cubic yards	2.8 million cubic yards*	2%
Water Treated	12,852,000 gallons	3 billion gallons*	14%
Wetlands Improved	0 acres	50 acres*	59%
Plants, Shrubs, Trees Planted**	6,000	1.1 million*	16%

\*Estimated totals

\*\*Does not include 400,000 shrub willows

## Onondaga Lake Dredging and Capping Progress

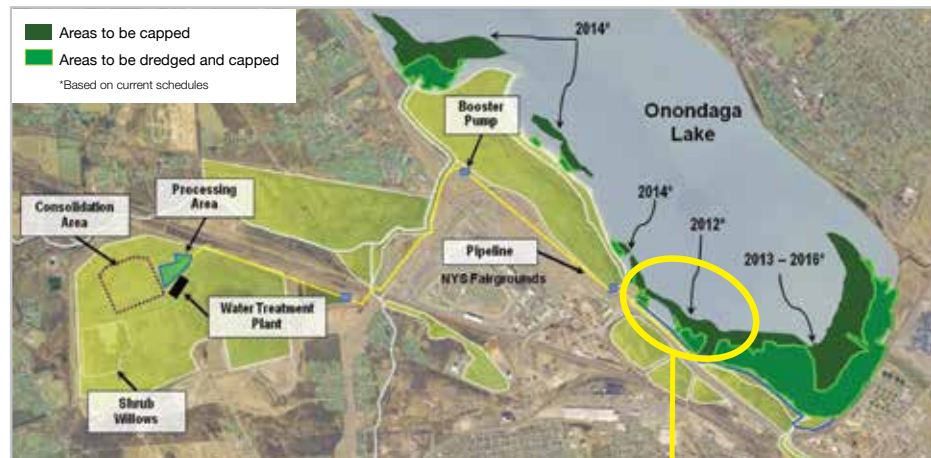

**Honeywell**

For more information, please contact Honeywell at 315.552.9784, or visit [www.lakecleanup.com](http://www.lakecleanup.com).
