

A large blue and white barge is on the water, carrying a large blue crane. The barge has 'Honeywell' and 'Berthoud' logos on its side. The crane is a large blue lattice boom crane. The barge is moving on a body of water with a forested shoreline in the background.

117,000 cubic yards of lake material removed.



121,766,000 gallons of water treated.



54,700 cubic yards of capping material placed.



1,600 plants, shrubs, and trees planted.

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in July 2013	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	117,000 cubic yards	2 million cubic yards*	30.6%
Cap Material Placed	54,700 cubic yards	2.8 million cubic yards*	7.8%
Water Treated	121,766,000 gallons	3 billion gallons*	30%
Wetlands Improved	0 acres	50 acres*	63%
Plants, Shrubs, Trees Planted**	1,600	1.1 million*	18%

**Does not include 400,000 shrub willows

■ Areas to be capped
■ Areas to be dredged and capped

*Based on current schedules

Onondaga Lake

2014*

Booster Pump

Consolidation Area

Processing Area

Water Treatment Plant

Shrub Willows


Pipeline

NYS Fairgrounds

2014*

2012*

2013 - 2016*

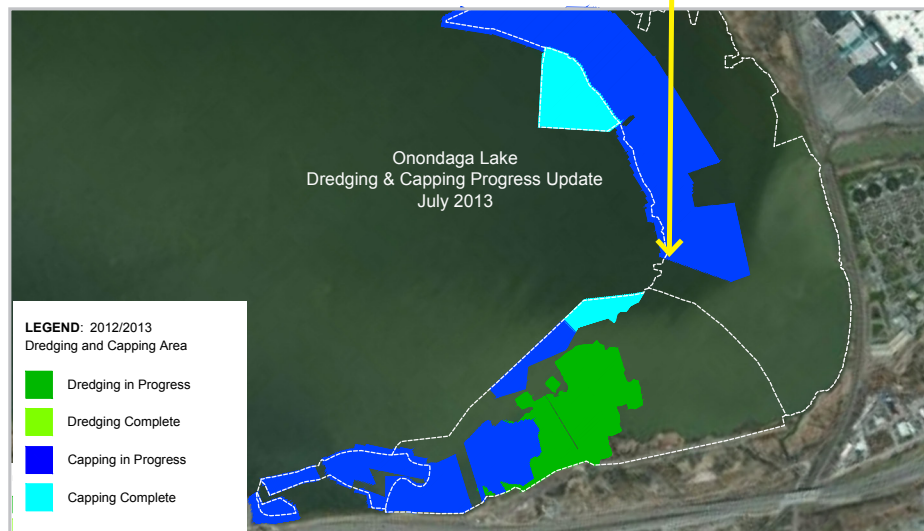

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
