

JULY 2014 HIGHLIGHTS



DREDGING

150,000 cubic yards of lake material removed.



WATER TREATED

136,000,000 gallons of water treated.



CAPPING

150,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS

11,000 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

JULY 1 – JULY 31, 2014

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in July 2014	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	150,000 cubic yards	2 million cubic yards*	83%
Cap Material Placed	150,000 cubic yards	2.8 million cubic yards*	33%
Water Treated	136,000,000 gallons	2.8 – 3.1 billion gallons*	83%
Wetlands Improved	1 acre	50 acres*	73%
Plants, Shrubs, Trees Planted**	11,000 plants	1.1 million*	27%

*Estimated totals

**Does not include 400,000 shrub willows


Onondaga Lake Dredging and Capping Progress

LEGEND 2012/2013/2014

■ Dredging in Progress

■ Dredging Complete

--- Dredge Areas

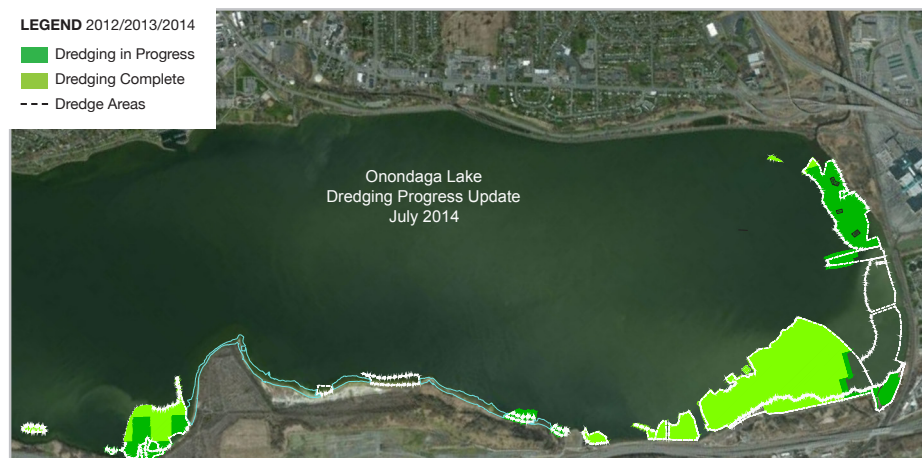


LEGEND 2012/2013/2014

■ Capping in Progress

■ Capping Complete

--- Cap Areas

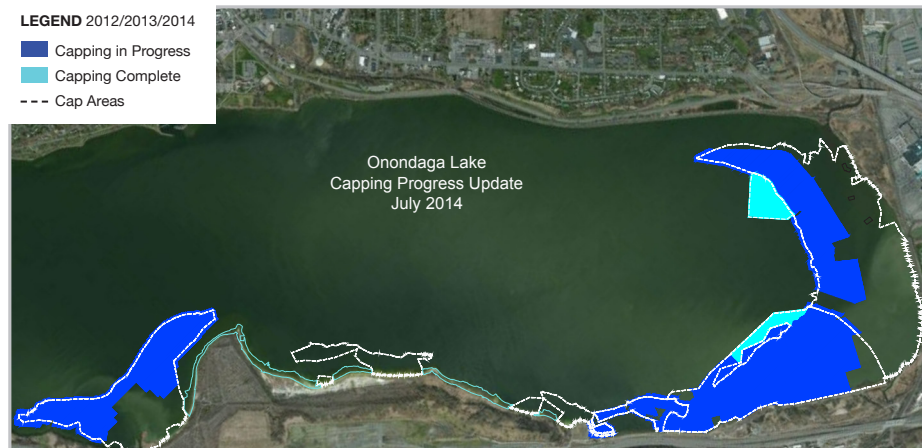

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
