

JULY 2016 HIGHLIGHTS



DREDGING
Completed



WATER TREATED
Completed



CAPPING
75,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS
87,545 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

JULY 1 – JULY 31, 2016

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

| Major Projects | Progress in July 2016 | Project Total | % Complete To Date |
|---------------------------------|-----------------------|---------------------------|--------------------|
| Barrier Wall | Complete | 1.5 miles | 100% |
| Pipeline | Complete | 3.9 miles | 100% |
| Water Treatment Plants | Complete | 3 plants | 100% |
| LCP Chemicals Cleanup Site | Complete | 7 tons of mercury removed | 100% |
| Lake Material Removed | Complete | 2.2 million cubic yards | 100% |
| Cap Material Placed | 75,000 cubic yards | 3.07 million cubic yards* | 98% |
| Water Treated | Complete | 2.46 billion gallons | 100% |
| Wetlands Improved | 9.5 acres | 87 acres* | 81% |
| Plants, Shrubs, Trees Planted** | 87,545 plants | 1.1 million* | 53% |

*Estimated totals

**Does not include 750,000 shrub willows

Onondaga Lake Dredging and Capping Progress

LEGEND 2012/2013/2014

■ Dredging in Progress

■ Dredging Complete

--- Dredge Areas




LEGEND 2012/2013/2014/2015/2016

■ Capping in Progress

■ Capping Complete

--- Cap Areas

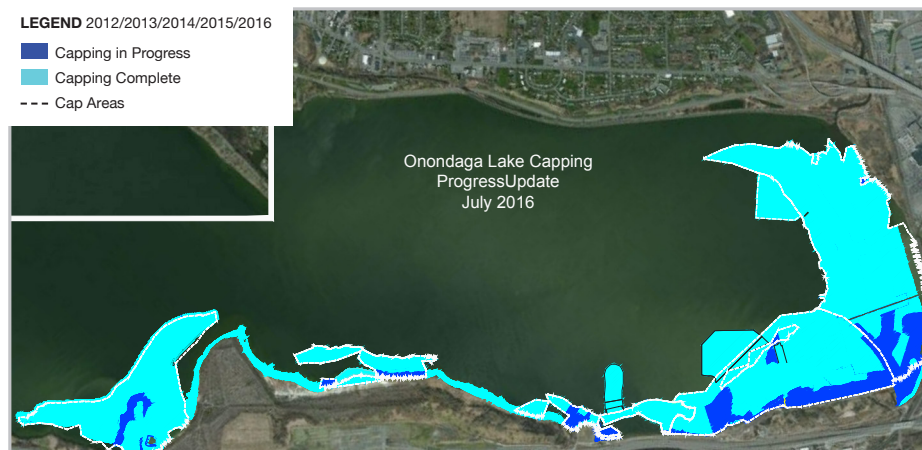

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
