

JUNE 2015 HIGHLIGHTS



DREDGING
Completed



WATER TREATED
Completed



CAPPING
100,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS
41,400 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

JUNE 1 – JUNE 30, 2015

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in June 2015	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	Complete	2.2 million cubic yards	100%
Cap Material Placed	100,000 cubic yards	2.8 million cubic yards*	70%
Water Treated	Complete	2.46 billion gallons	100%
Wetlands Improved	4.8 acres	87 acres*	57%
Plants, Shrubs, Trees Planted**	41,400 plants	1.1 million*	35%

*Estimated totals

**Does not include 750,000 shrub willows

Onondaga Lake Dredging and Capping Progress

LEGEND 2012/2013/2014

■ Dredging in Progress

■ Dredging Complete

--- Dredge Areas




LEGEND 2012/2013/2014/2015

■ Capping in Progress

■ Capping Complete

--- Cap Areas

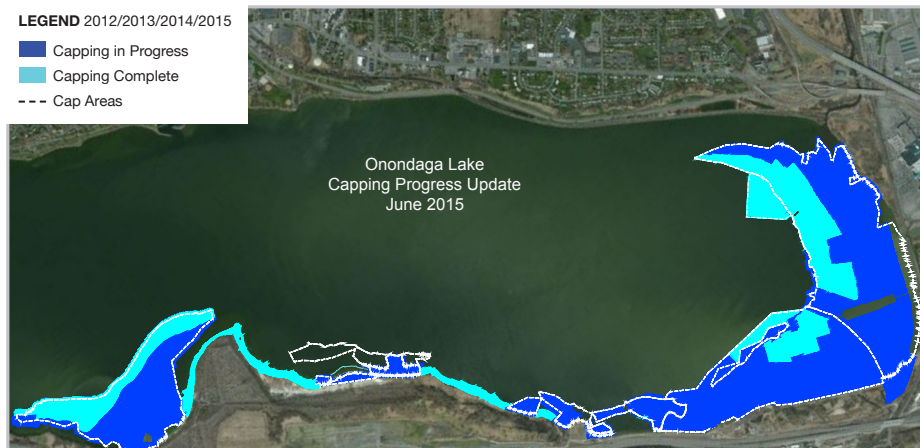

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
