

## OCTOBER 2013 HIGHLIGHTS



### DREDGING

190,000 cubic yards of lake material removed.



### WATER TREATED

147,759,000 gallons of water treated.



### CAPPING

80,000 cubic yards of capping material placed.



### HABITAT / PLANTS / WETLANDS

11,600 plants, shrubs, and trees planted.

## Onondaga Lake Cleanup Progress

OCTOBER 1 – OCTOBER 31, 2013



Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in October 2013	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	190,000 cubic yards	2 million cubic yards*	54%
Cap Material Placed	80,000 cubic yards	2.8 million cubic yards*	16%
Water Treated	147,759,000 gallons	3 billion gallons*	45%
Wetlands Improved	1 acre	50 acres*	64%
Plants, Shrubs, Trees Planted**	11,600	1.1 million*	19%

\*Estimated totals

\*\*Does not include 400,000 shrub willows

## Onondaga Lake Dredging and Capping Progress

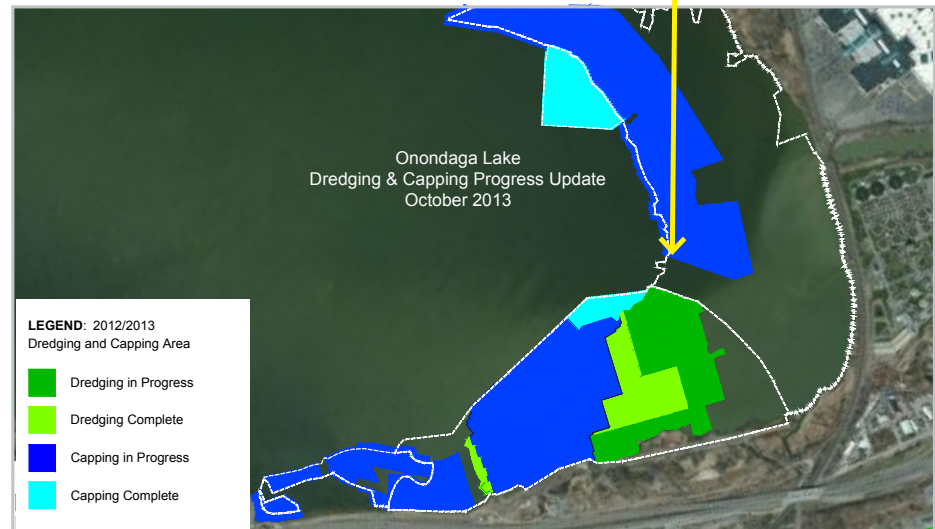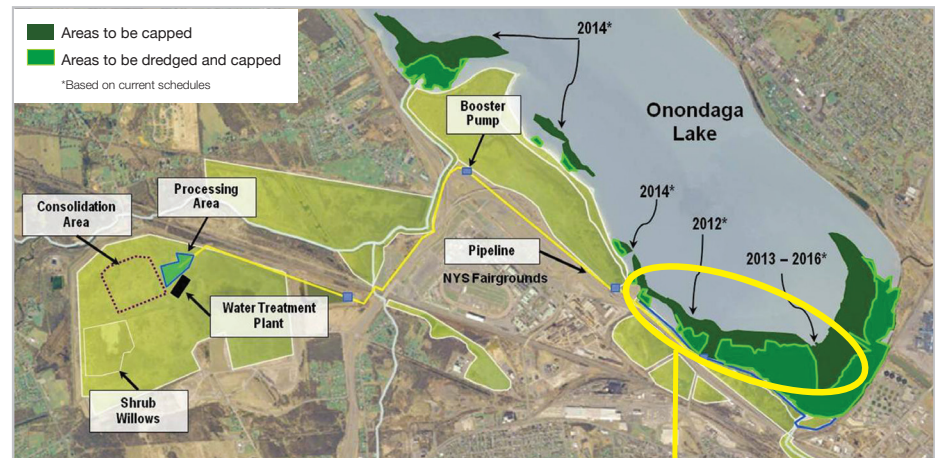

**Honeywell**

For more information, please contact Honeywell at 315.552.9784, or visit [www.lakecleanup.com](http://www.lakecleanup.com).
