

OCTOBER 2014 HIGHLIGHTS



DREDGING

255,000 cubic yards of lake material removed.



WATER TREATED

147,000,000 gallons of water treated.



CAPPING

240,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS

500 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

OCTOBER 1 – OCTOBER 31, 2014

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in October 2014	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	255,000 cubic yards	2.175 million cubic yards	100%
Cap Material Placed	240,000 cubic yards	2.8 million cubic yards*	55%
Water Treated	147,000,000 gallons	2.46 billion gallons	100%
Wetlands Improved	0 acres	50 acres*	74%
Plants, Shrubs, Trees Planted**	500 plants	1.1 million*	28%

*Estimated totals

**Does not include 400,000 shrub willows

Onondaga Lake Dredging and Capping Progress

LEGEND 2012/2013/2014

■ Dredging in Progress

■ Dredging Complete

--- Dredge Areas




LEGEND 2012/2013/2014

■ Capping in Progress

■ Capping Complete

--- Cap Areas

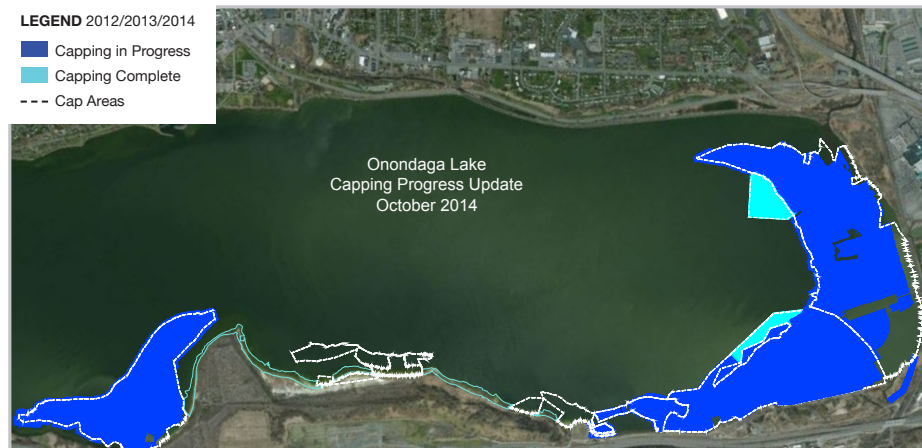

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
