

SEPTEMBER 2014 HIGHLIGHTS



DREDGING

120,000 cubic yards of lake material removed.



WATER TREATED

139,000,000 gallons of water treated.



CAPPING

180,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS

0 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

SEPTEMBER 1 – SEPTEMBER 30, 2014

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in September 2014	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	120,000 cubic yards	2 million cubic yards*	96%
Cap Material Placed	180,000 cubic yards	2.8 million cubic yards*	47%
Water Treated	139,000,000 gallons	2.8 – 3.1 billion gallons*	96%
Wetlands Improved	0 acres	50 acres*	74%
Plants, Shrubs, Trees Planted**	0 plants	1.1 million*	28%

*Estimated totals

**Does not include 400,000 shrub willows


Onondaga Lake Dredging and Capping Progress

LEGEND 2012/2013/2014

■ Dredging in Progress

■ Dredging Complete

--- Dredge Areas

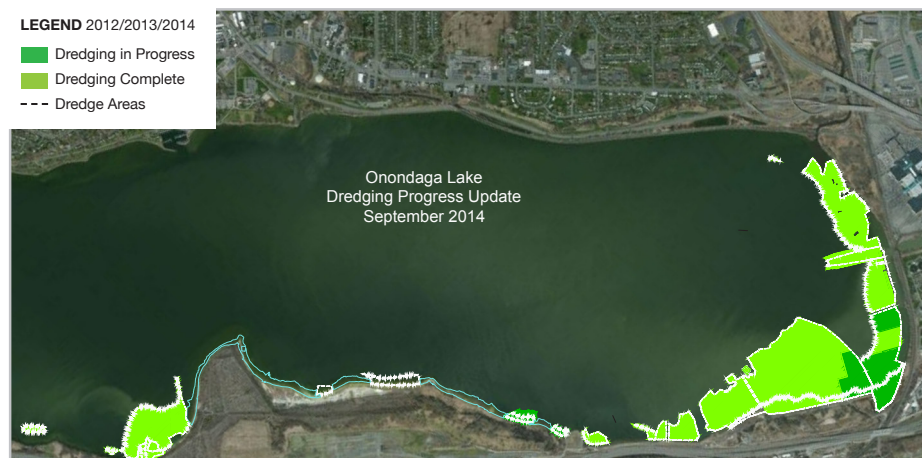


LEGEND 2012/2013/2014

■ Capping in Progress

■ Capping Complete

--- Cap Areas

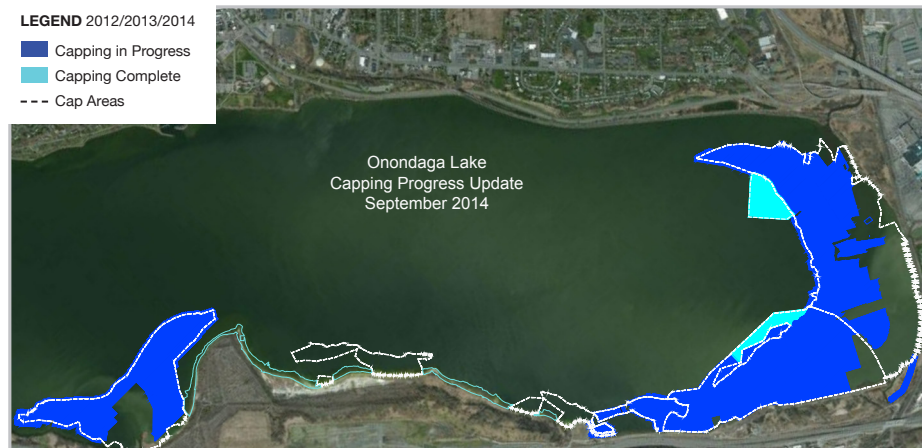

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
